
Rolled-up Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
Barnstable Superior Court Project - Baseline Schedule - Rev. 00 - 07.21.26		266	14-May-26	02-Jun-27
Key Dates & Milestones		266	14-May-26	02-Jun-27
MS-1000	Notice to Proceed	0	14-May-26	
MS-1030	Substantial Completion	0		10-May-27
MS-1040	Final Completion	0		02-Jun-27
Interim Milestones		93	30-Nov-26	15-Apr-27
Pre-Construction		89	14-May-26	16-Sep-26
Submittals		75	14-May-26	27-Aug-26
Approvals		14	28-Aug-26	16-Sep-26
Permits		76	14-May-26	28-Aug-26
Procurement		85	31-Jul-26	29-Nov-26
Construction		203	15-Jul-26	04-May-27
Mobilization & Prep Work		48	15-Jul-26	18-Sep-26
GC-130	Construct Masonry Repair Mockups	33	15-Jul-26	28-Aug-26
EXP-100	Perform Exploratory Demolition	3	15-Jul-26	17-Jul-26
EXP-110	Conduct On-Site Material Sampling	20	20-Jul-26	14-Aug-26
NEL-1080	Field Measure Windows	7	20-Jul-26	28-Jul-26
EXP-120	Obtain Lab Results & Finalize Abatement Scope	5	17-Aug-26	21-Aug-26
GC-100	Mobilize to Site & Establish Laydown	6	31-Aug-26	07-Sep-26
GC-120	Install Temporary Facilities & Dust Controls	10	31-Aug-26	11-Sep-26
ABT-010	Perform Grass Abatement, Site Pre-Clean & Vacuuming	10	07-Sep-26	18-Sep-26
Scaffolding		112	07-Sep-26	16-Feb-27
NEL-100	Erect Scaffold - North	10	07-Sep-26	18-Sep-26
SEL-100	Erect Scaffold - South	10	07-Sep-26	18-Sep-26
EEL-100	Erect Scaffold - East	10	06-Nov-26	19-Nov-26
WEL-100	Erect Scaffold - West	10	02-Feb-27	16-Feb-27
Abatement, Trim & Exterior Painting		69	21-Sep-26	28-Dec-26
Abatement, Trim & Exterior Painting - North Elevation		39	21-Sep-26	12-Nov-26
Abatement		10	21-Sep-26	02-Oct-26
Wood Trim		14	19-Oct-26	05-Nov-26
Exterior Painting		29	05-Oct-26	12-Nov-26
Abatement, Trim & Exterior Painting - East Elevation		31	05-Oct-26	16-Nov-26
Abatement		12	05-Oct-26	20-Oct-26
Wood Trim		14	21-Oct-26	09-Nov-26
Exterior Painting		5	10-Nov-26	16-Nov-26
Abatement, Trim & Exterior Painting - South Elevation		33	21-Oct-26	07-Dec-26
Abatement		12	21-Oct-26	05-Nov-26
Wood Trim		14	10-Nov-26	30-Nov-26
Exterior Painting		5	01-Dec-26	07-Dec-26
Abatement, Trim & Exterior Painting - West Elevation		35	06-Nov-26	28-Dec-26
Abatement		12	06-Nov-26	23-Nov-26
Wood Trim		14	01-Dec-26	18-Dec-26
Exterior Painting		5	21-Dec-26	28-Dec-26
Masonry		104	23-Sep-26	22-Feb-27
Masonry Cleaning - South Elevation		10	23-Sep-26	06-Oct-26
Masonry Repointing & Repair - South Elevation		26	07-Oct-26	11-Nov-26
Masonry Cleaning - West Elevation		10	24-Nov-26	08-Dec-26

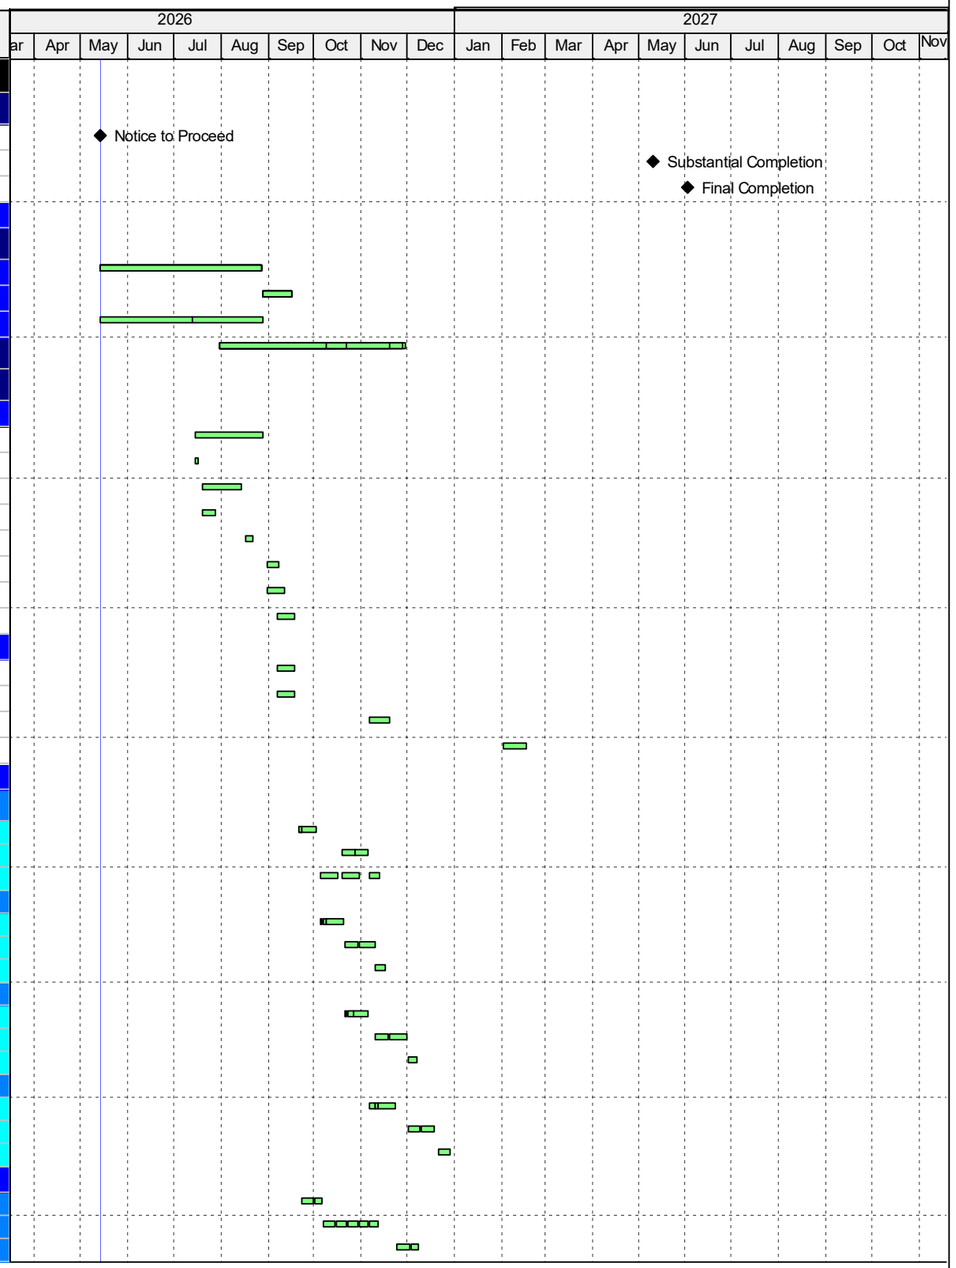

Start: 14-May-26
Finish: 02-Jun-27
Data Date: 14-May-26

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Milestone

Barnstable Superior Court Project - Baseline Schedule - Rev. 00 - 07.21.26
Page 1 of 2


HOMER CONTRACTING

Prepared By:A.E

Date	Revision	Checked	Approved
21-Jul-26	00		

Rolled-up Schedule Layout

Activity ID	Activity Name	Original Duration	Start	Finish
	Masonry Repointing & Repair - West Elevation	26	09-Dec-26	15-Jan-27
	Masonry Cleaning - North Elevation	10	11-Dec-26	24-Dec-26
	Masonry Repointing & Repair - North Elevation	26	28-Dec-26	03-Feb-27
	Masonry Cleaning - East Elevation	10	30-Dec-26	13-Jan-27
	Masonry Repointing & Repair - East Elevation	26	14-Jan-27	22-Feb-27
	Concrete Stairs, Ramps & Site	23	01-Apr-27	04-May-27
	Foundation & Basement Masonry	38	07-Oct-26	30-Nov-26
	Shoring & Stabilization	15	07-Oct-26	27-Oct-26
	Pier & Arch Rebuilding	19	28-Oct-26	23-Nov-26
	Wall Repointing & Crack Repair	23	28-Oct-26	30-Nov-26
	Parapet, Cornice & Sheet Metal (Roofing)	34	23-Oct-26	10-Dec-26
	Parapet, Cornice & Sheet Metal - South Elevation	16	23-Oct-26	13-Nov-26
	Parapet, Cornice & Sheet Metal - West Elevation	16	02-Nov-26	23-Nov-26
	Parapet, Cornice & Sheet Metal - North Elevation	16	10-Nov-26	02-Dec-26
	Parapet, Cornice & Sheet Metal - East Elevation	16	18-Nov-26	10-Dec-26
	Window Replacement	109	26-Oct-26	02-Apr-27
	Window Replacement - North Elevation	62	26-Oct-26	25-Jan-27
	Window Replacement - East Elevation	62	11-Nov-26	10-Feb-27
	Window Replacement - South Elevation	62	30-Nov-26	01-Mar-27
	Window Replacement - West Elevation	62	04-Jan-27	02-Apr-27
	Doors	19	05-Apr-27	30-Apr-27
	Doors - South Elevation	7	05-Apr-27	13-Apr-27
	Doors - West Elevation	4	14-Apr-27	20-Apr-27
	Doors - North Elevation	4	21-Apr-27	26-Apr-27
	Doors - East Elevation	4	27-Apr-27	30-Apr-27
	Testing & Commissioning	25	05-Apr-27	10-May-27
	Close-Outs	16	11-May-27	02-Jun-27

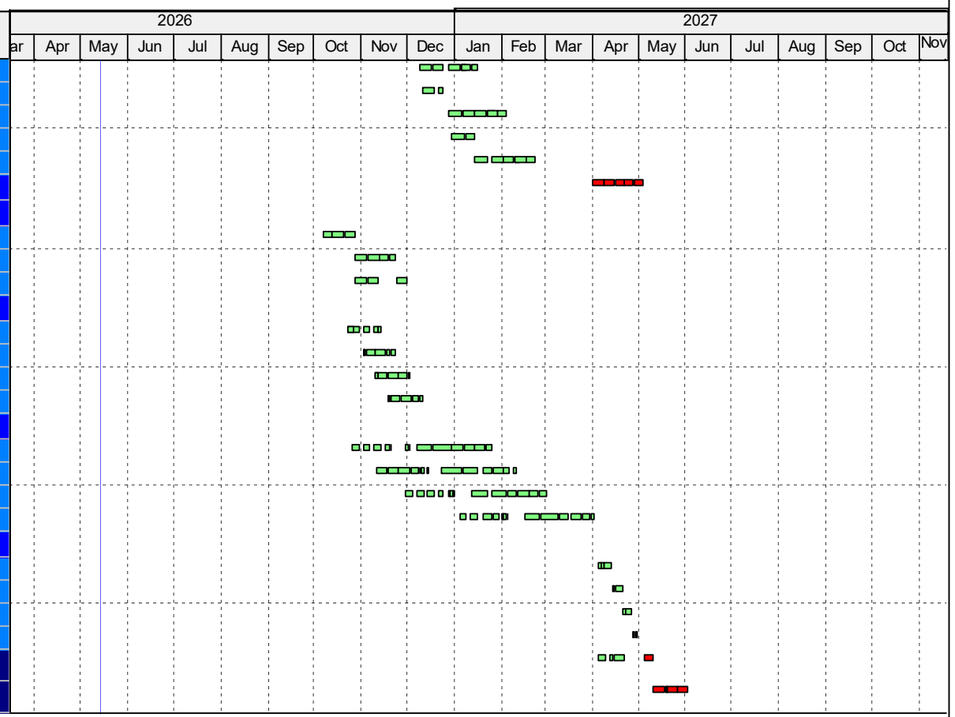

Start: 14-May-26
Finish: 02-Jun-27
Data Date: 14-May-26

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...
Milestone

Barnstable Superior Court Project - Baseline Schedule - Rev. 00 - 07.21.26

HOMER CONTRACTING

Prepared By:A.E

Date	Revision	Checked	Approved
21-Jul-26	00		
